

Request for Conduit— Joint Opportunity



Date: _____	Approx. Project Length: _____
Contractor: _____	Project Start Date: _____
Owner Name: _____	Contractor Contact: (P) () _____ - _____
Site Address: _____	Owner Info: Email _____
_____	(P) () _____ - _____


All Rock Island Communication Facilities are furnished at the Customers expense. Using Rock Island Material ensures that the facilities installed are not proprietary and can be located. Total material and handling costs are billed after delivery. Payment for these items does not constitute ownership or exclusive rights to materials or services provided by Rock Island Communications. A request for quote of materials and labor can be obtained by completing this form and checking the appropriate box below.

Sketch of Proposed Route/ Or See Attached Map

An accurate sketch is need to determine the product and location of facilities. www.sjcgis.org provides Draw and Print functions.

<p>Please Provide Quote Prior to Installation <input type="checkbox"/></p> <p>Send Quote to: (Email) _____</p> <p>Attention: _____</p>	<p style="text-align: center;">Rock Island Use Only</p> <p>Completed Date: _____</p> <p>Completed By: _____</p> <p>Project Number: _____</p>
---	---

(Example of attached map) Using www.sjcgis.org

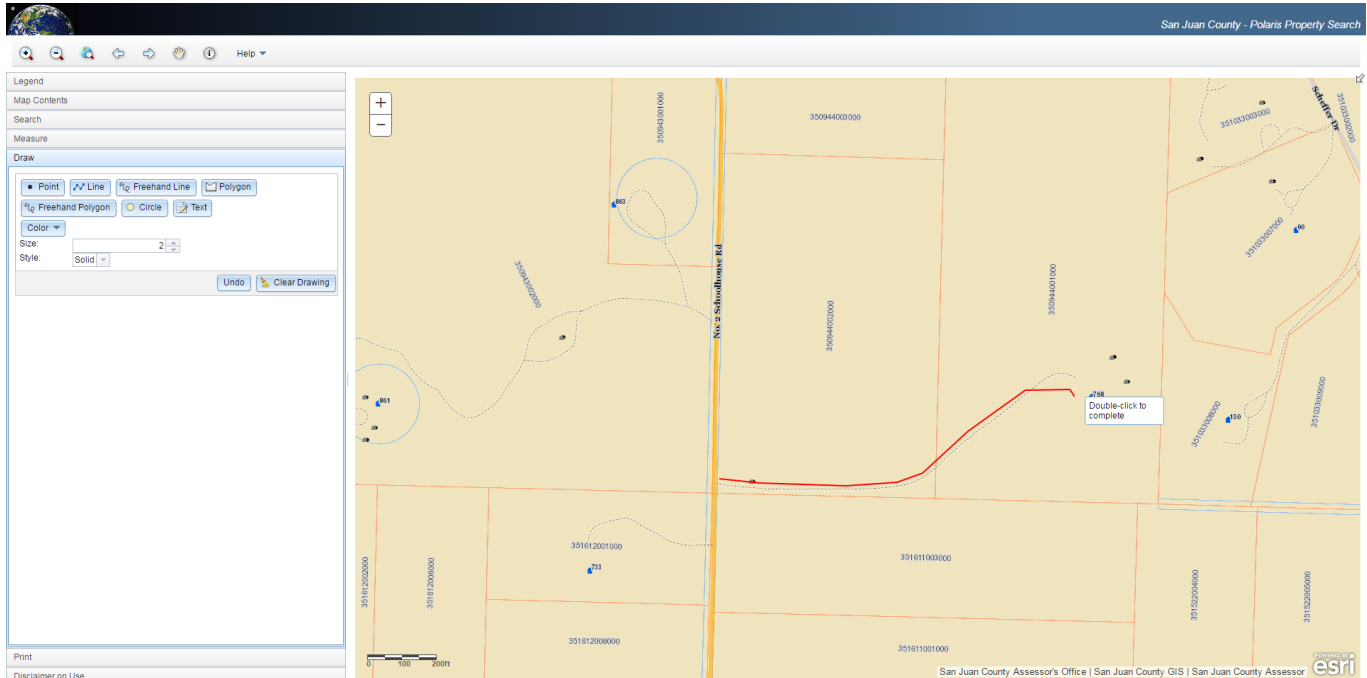

Owner Furnished Conduit

Owners/Contractors can install their own facilities for future fiber use if preferred. Rock Island Requirements for Owner Furnished Conduit are:

- 1" Grey PVC Sch 40 or greater
- Continuous runs no longer than 1000'
- No more than (4) 90 deg bends per run
- Terminated at project or extends above ground
- Jet Line Installed (if no jet line is installed, Rock island can proof and install jet line for \$.50/ft.
- Terminated on exterior of building at point of entry.

Contractors Notes for installing Rock island Microduct:

- Min depth of cover 18"
- Avoid over compaction of Microduct. Preferred min lift of 10"
- Leave 2-4' of exposed Microducts at designated points for vaulting or intercepts.
- Maintain 4' clearance from other utilities at stub or vault locations.
- Bedding should be free of large rocks and ensure smooth placement of Microduct

Any other construction related questions please email build@rockisland.com or call us at 378-5884
